

**GEORGETOWN TRANSPORTATION ENHANCEMENT CORPORATION
AGENDA ITEM COVER SHEET**

SUBJECT: September 2019 GTEC Updates - Wesley Wright, P.E., Systems Engineering Director/Michael Hallmark, CIP Manager

ITEM SUMMARY:

Northwest Boulevard:

Pre-con held on Nov 16th, Construction survey complete, ROW prep underway, NTP to be issued when Electric cleared

3rd Quarter 2020 expected completion

Rabbit Hill Road Improvements:

Design is tentatively complete. ROW procurement ongoing. Project limits have changed to end at the first property line North of Commerce Blvd on the East side of Rabbit Hill Rd.

Rivory Boulevard Extension:

Rivory, Williams to Northwest substantially complete. Road opened to traffic 9-3-19 from Williams to Park traffic circle. Section from Park to Northwest to be opened when construction on the Northwest project will allow.

Southeast Inner loop/ Southwestern Blvd

Southwestern:

- Turned in preliminary alignment of the roadway (30%) for review and comment.
- Performing Hydrologic and Hydraulic calculations.

SE Inner Loop:


- Finalizing horizontal alignment
- Preparing constraints map

Performing hydrologic and hydraulic calculations.

ROW needs on Southwestern to be determined

**Northwest Boulevard
(Fontana Drive to Austin Avenue)
Project No. 5QX TIP No. AF
September 2019**

Project Description	Construction of overpass and surface roads to connect Northwest Boulevard with Austin Avenue and FM 971.
Purpose	This project will relieve congestion at the Austin Avenue/Williams Drive intersection and provide a more direct access from the west side of IH 35 corridor to Georgetown High School and SH 130 via FM 971.
Project Manager	Joel Weaver and Wesley Wright, P.E.
Engineer	Klotz Associates

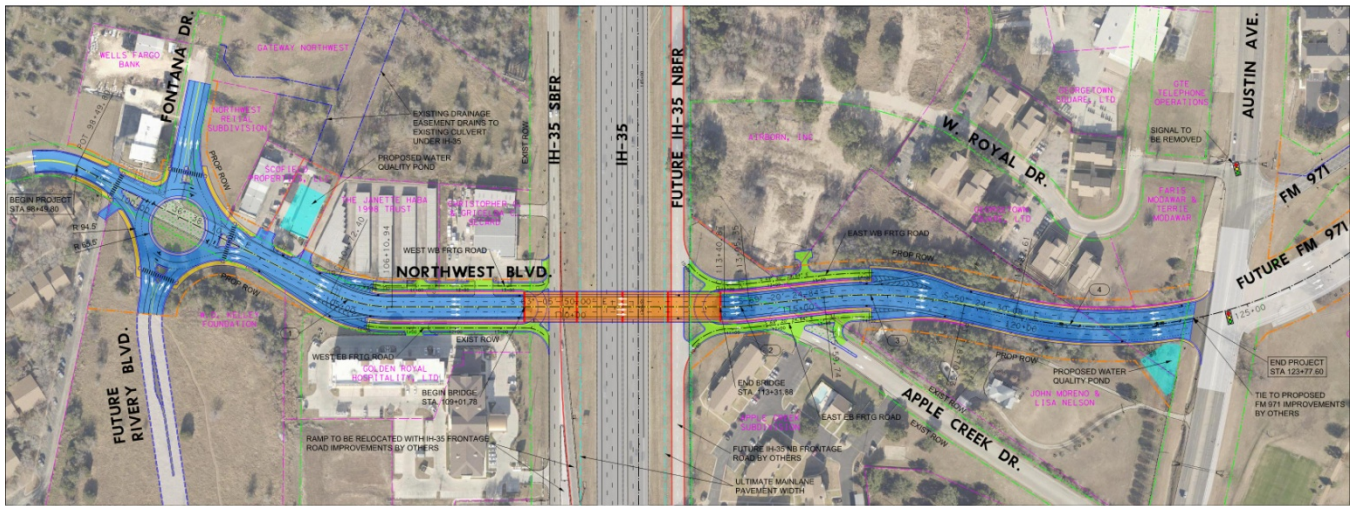


Element	Status / Issues
Design	Design is complete.
Environmental/ Archeological	Complete
Rights of Way	Offers have been made on 9 parcels. 9 parcels needed, 7 acquired to date, 2 in condemnation with constructive possession obtained.
Utility Relocations	TBD
Construction	Pre-con held on Nov 16 th , Construction survey complete, ROW prep underway, NTP to be issued when Electric cleared 3 rd Quarter 2020 expected completion.
Other Issues	

Rabbit Hill Road Improvements Project
(Westinghouse Road to S. Clearview Drive)
Project No. 5RQ TIP No. BZ
September 2019

Project Description Reconstruct Rabbit Hill Road from Westinghouse Road northward to S. Clearview Dr. Widening along Westinghouse Road will also be included in the schematic for additional turning lanes to/from Westinghouse Road. The project length along the anticipated alignment is approximately 0.75 miles

Project Managers Ken Taylor and Wesley Wright, P.E.

Engineer CP&Y, Inc.

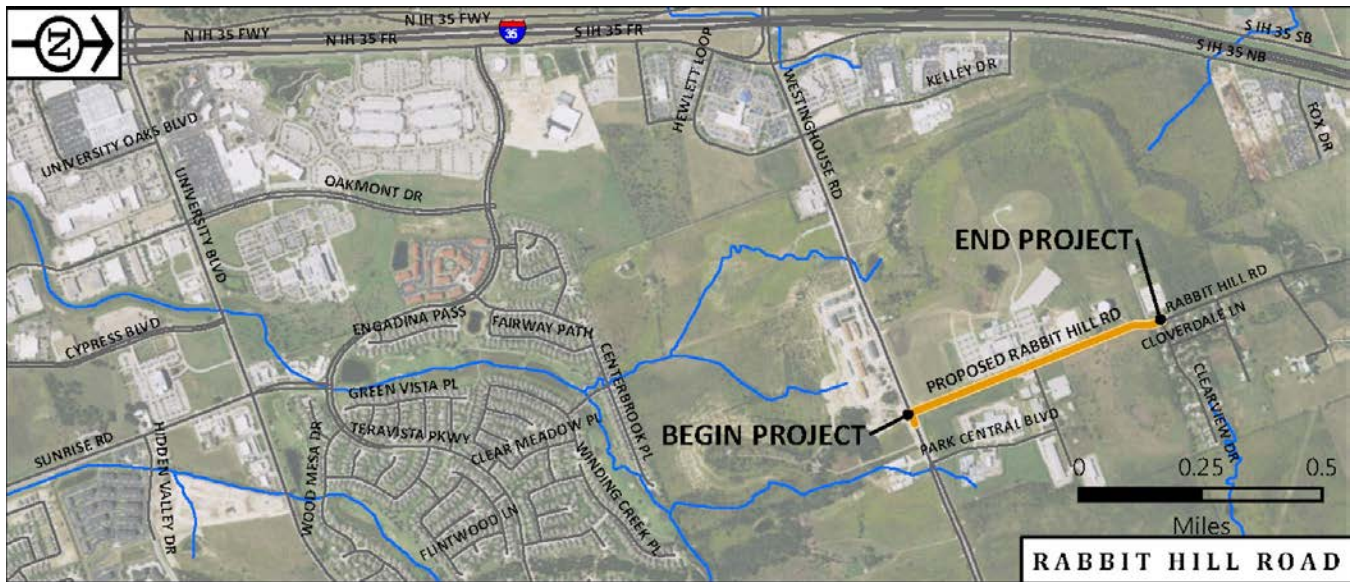


Element	Status / Issues		
Design	Final Design Tentatively complete.		
Environmental/ Archeological	Efforts underway and any issues are expected to be identified in the coming month.		
Rights of Way	Two properties acquired as part of Mays St. Extension. Two remaining, negotiations ongoing and Council has approved condemnation.	Total Parcels:	4
		Possession:	2
		Pending:	2
Utility Relocations	Will be initiated as ROW/easements are acquired and as part of the bidding process. Multiple relocations expected – Round Rock water and Georgetown Electric.		
Construction	ROW procurement ongoing		
Other Issues	Project limits have changed to end at the first property line North of Commerce Blvd on the East side of Rabbit Hill Rd.		

**Widening of: SE Inner Loop - FM 1460 to Austin Avenue Roadway &
Southwestern Boulevard – Raintree Drive to SE Inner Loop Roadway**
Project No.
September 2019

Project Description FM 1460 to Austin Avenue Roadway Widening Project & Southwestern Boulevard – Raintree Drive to SE Inner Loop Roadway Widening Project (See Attached Exhibit C). The professional services will consist of providing final roadway, drainage, water, wastewater, incidental designs, as well as, utility coordination, ROW support, environmental phase I investigations, archeological investigations, geotechnical investigations, ROW & Temporary Construction Easement (TCE) metes and bounds documents, bidding documents, bidding services, and construction administration services.

Project Managers Joel Weaver and Wesley Wright, P.E.

Engineer KPA & Associates

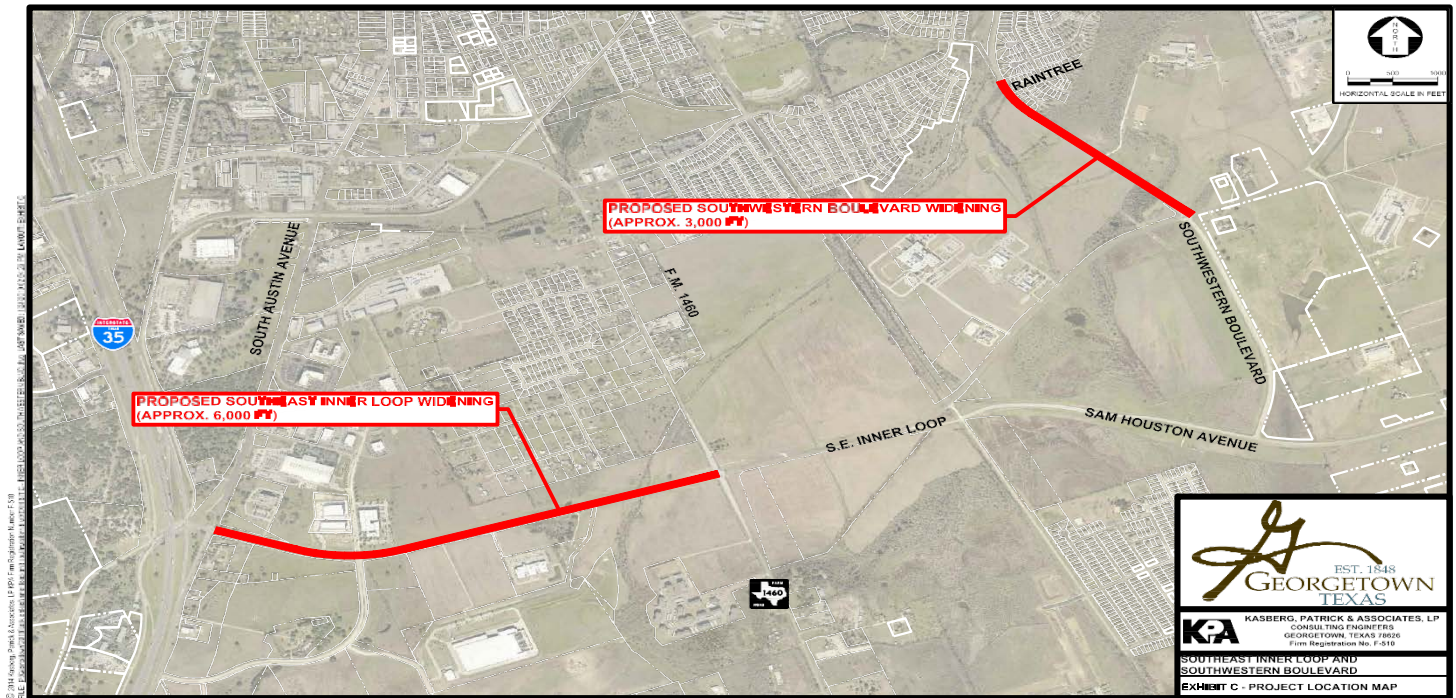

Element	Status / Issues		
Design	Southwestern:		
	<ul style="list-style-type: none"> Turned in preliminary alignment of the roadway (30%) for review and comment. Performing Hydrologic and Hydraulic calculations. 		
Environmental/ Archeological	SE Inner Loop:		
	<ul style="list-style-type: none"> Finalizing horizontal alignment Preparing constraints map Performing hydrologic and hydraulic calculations. 		
Efforts to begin April 2019 and any issues are expected to be identified in the coming month.			
Rights of Way	ROW needs on Southwestern to be determined	Total Parcels:	0
		Possession:	0
		Pending:	0
Utility Relocations	To be determined		
Construction			

Other Issues	None.
---------------------	-------


Rivory Boulevard Extension
(Williams Drive to Northwest Boulevard @ Fontana Drive)
Project No. 5RM TIP No. AD
September 2019

Project Description Develop the Rights-of-Way Map, acquire ROW, address potential environmental issues and complete construction plans specifications and estimate (PS&E) for the extension of Rivory Boulevard from Williams Drive to Northwest Boulevard at Fontana Drive in anticipation of future funding availability.

Purpose To provide a route between Williams Drive and Northwest Boulevard serving the Gateway area, providing an alternate route from Williams Drive to the future Northwest Boulevard Bridge over IH 35, to provide a route between the hotels in the Gateway area and the proposed Conference Center near Rivory Boulevard and Wolf Ranch Parkway.

Project Manager Travis Baird, Joel Weaver, and Wesley Wright, P.E.

Engineer Kasberg Patrick and Associates

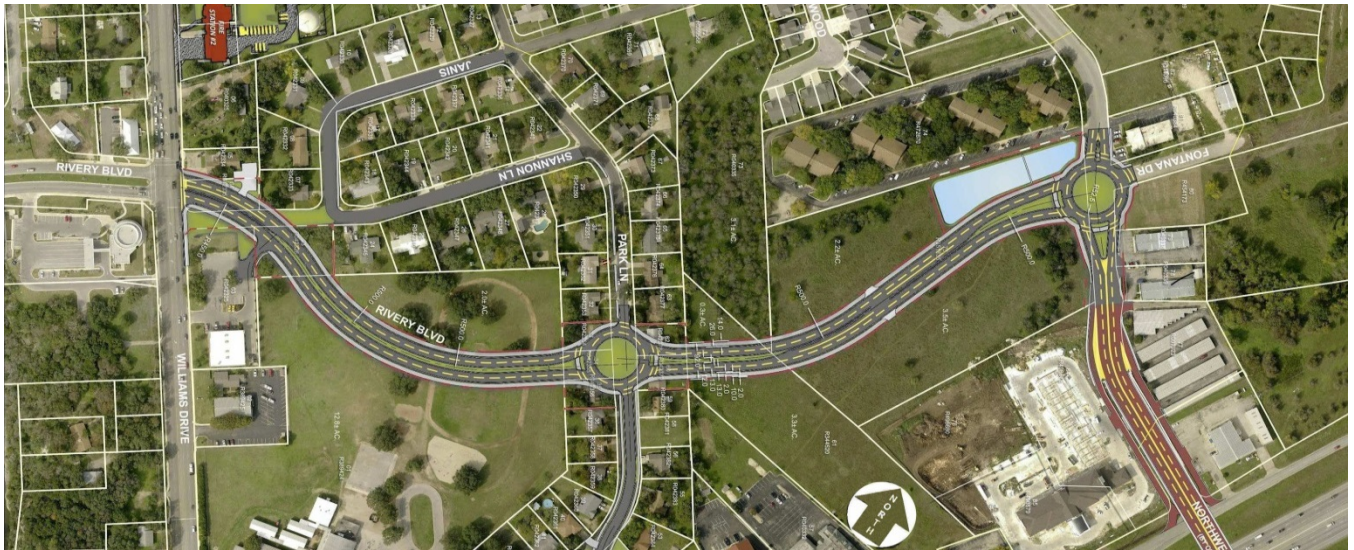

Element	Status / Issues		
Design	Complete		
Environmental/ Archeology	Complete		
Rights of Way	All parcels in possession. Condemnation of 1 parcel continuing, no impact on operation of roadway.	Total Parcels:	22
		Appraised:	22
		Offers:	22
		Acquired:	21
		Closing pending:	0
		Condemnation:	1
Utility Relocations	Complete		
Construction	Rivory, Williams to Northwest substantially complete. Road opened to traffic 9-3-19 from Williams to Park traffic circle. Section from Park to Northwest to be opened when construction on the Northwest project will allow.		
Other Issues			
